

In-Progress Line Status

○ Next 15 Days

○ Next 30 Days

○ Custom

● Delayed

Upcoming Time

Calendar icon

Status

All

Asia

3

EU

13

LA

3

NA

13

Plant	# lines to cutover before date	First Cutover Date
Lima	11	28-Feb-23
Gebze	8	31-Dec-22
London	4	31-Oct-22
Cabuyao	3	06-Jan-23
Medellin	3	12-Jun-22
Alexandria	2	31-Mar-23
Amiens	1	07-Apr-23

Status

● ATC Config

● CDW Build

● Plant Validation in progress (Prod)

11

9

2

8

4

3

3

3

2

2

1

Lima

Gebze

London



Cabuyao

Medellin


Alexandria

Amiens


Mechelen



Platform

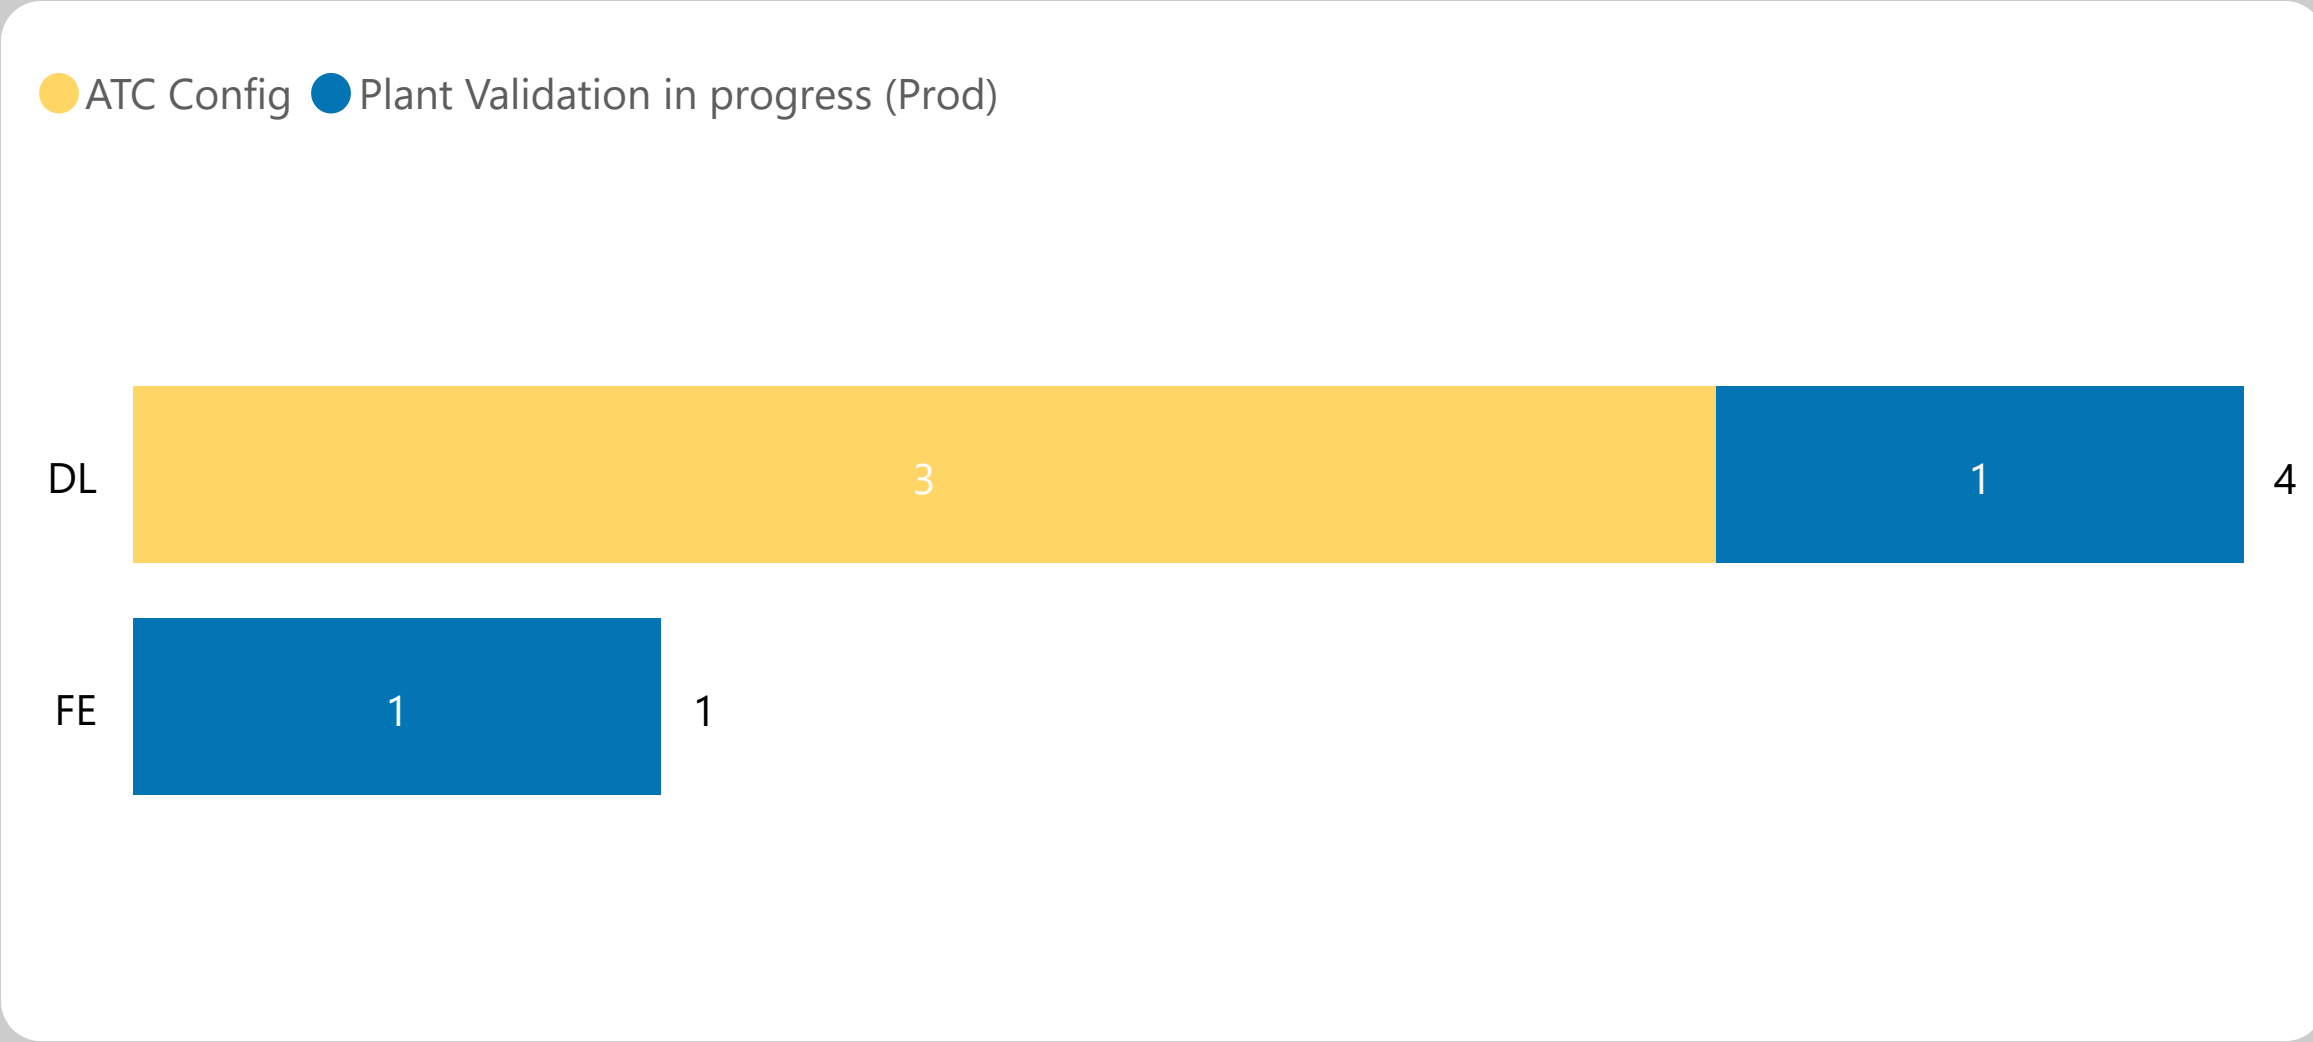

Region

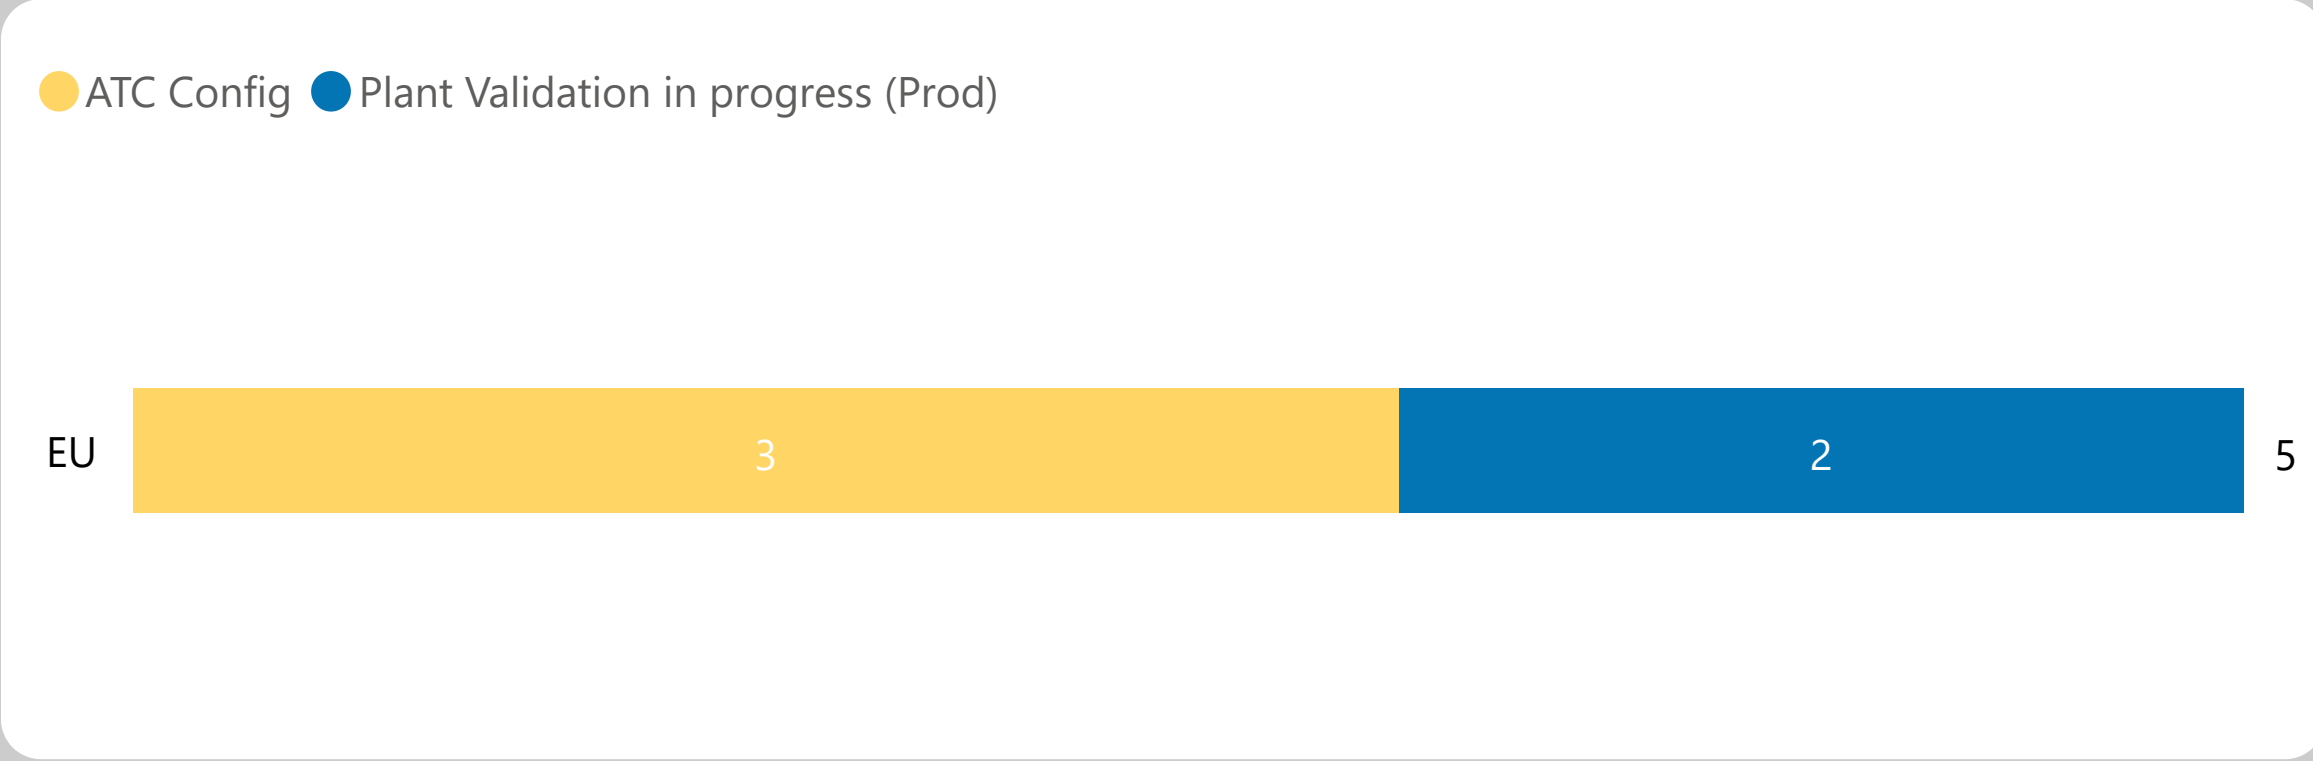

Plant

Plant	Line	Cutover Date	Status	CPS Status
London	PGLO-004	31-Oct-22	ATC Config	Blue
London	BBLO-203	09-Jan-23	Plant Validation in progress (Prod)	Blue
London	PGLO-007	31-May-23	ATC Config	Blue
London	MGLO Tower	30-Jun-23	Plant Validation in progress (Prod)	Blue
London	PGLO-005	30-Jun-23	ATC Config	Blue

Transition Health Check

Plant	Staffed	Capability	DTM Drumbeats	% Task Completed	Leadership Update	CPSUpdate	Engagement	DualEntry	Overall Score
St Louis	20 %	25 %	0 %	100 %	0 %	0 %	0 %	0 %	22 %
Lima	67 %	75 %	75 %	33 %	80 %	50 %	100 %	100 %	72 %
Gebze	70 %	100 %	100 %	75 %	75 %	100 %	100 %	100 %	88 %
Alexandria	80 %	100 %	20 %	0 %	0 %	0 %	80 %	100 %	52 %
Cabuyao	90 %	83 %	100 %	90 %	100 %	100 %	100 %	100 %	94 %
Gattatico	90 %	80 %	100 %	100 %	100 %	100 %	100 %	100 %	96 %
Amiens	100 %	100 %	100 %	100 %	50 %	75 %	100 %	66 %	87 %
Binh Duong	100 %	100 %	100 %	100 %	100 %	67 %	100 %	100 %	97 %
Chengdu	100 %	100 %	100 %	100 %	100 %	100 %	100 %	100 %	100 %
London	100 %	100 %	100 %	20 %	0 %	0 %	100 %	100 %	59 %
Moskva	100 %	100 %	100 %	50 %	100 %	25 %	100 %	100 %	70 %

Upcoming Time

6/30/2023

Status

All

Priority

All

Phase

All

CPS Risk

All

CR Status Overview

Platform	Plant	Change Request	Priority	Status	Due Date	Owner	Needed By	Committed	CPS Risk
		Comments visibility in OpsHub downtime table		New					No
		Connection between Proficy RTCR to CIL, SAP PM09, PROCTR, QW		New			2023-May-01		No
		Machine Stops KPI Development in iODS - Downtime report	2	Development		Alvaro	2023-Mar-01		No
		Mandatory comment upon selecting "No" in Activities		New					No
		PR Rate Loss + Scrap Loss Split for Filling Lines	2	New		Yaroslav			No
	BD	Adding Vietnamese Language Support		Assessment					No
ADW	Mechelen	Comment Visibility in OpsHub	3	Assessment		Hugh Oneil	2023-Aug-31		No
ADW	Mechelen	PO Comment Field in PE	3	Assessment		Geert	2023-Aug-31		No
ADW	Mechelen	TAMU Entry Opshub Simplification	3	Assessment		Hugh Oneil	2023-Jun-01		No
ADW	Mechelen	Workstation Driven Default View on Opshub	3	Assessment		Hugh Oneil	2023-Aug-30		No
All	All	Hypercare Sampling- 1. Extra	2	Assessment					No

Upcoming Time

6/18/2023

Criticality

All

Resolution (Days)

21

Open Issues

35

Issues Past Due Date

20


Issues Open > 2 Days

31


Issues Open > 1 Week

28

Issues By Site

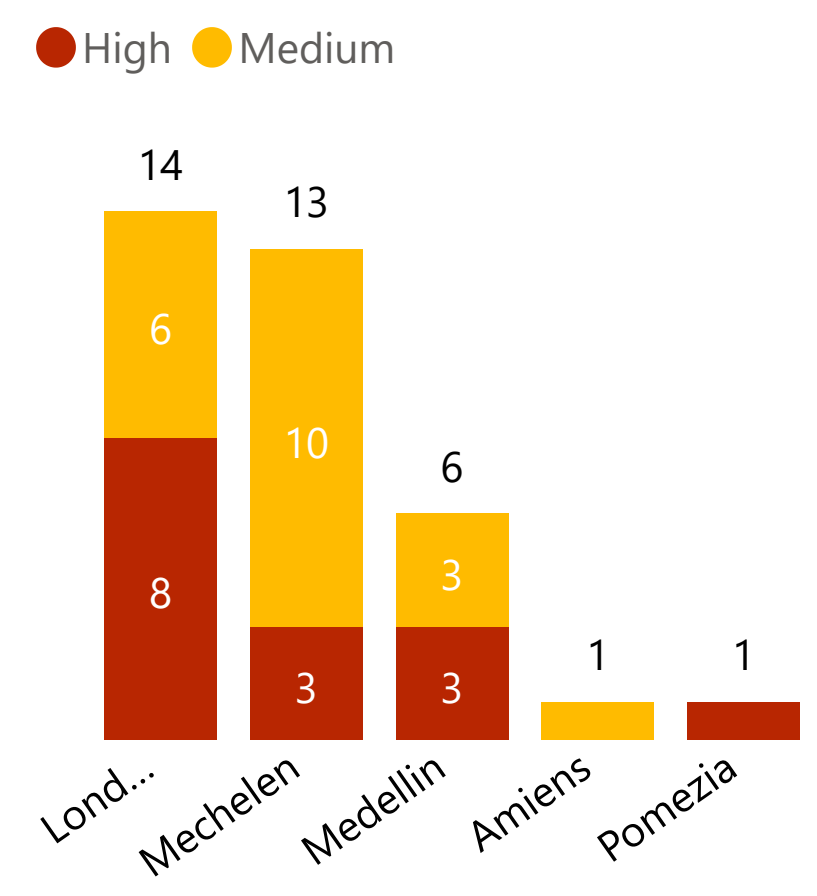

Support Team

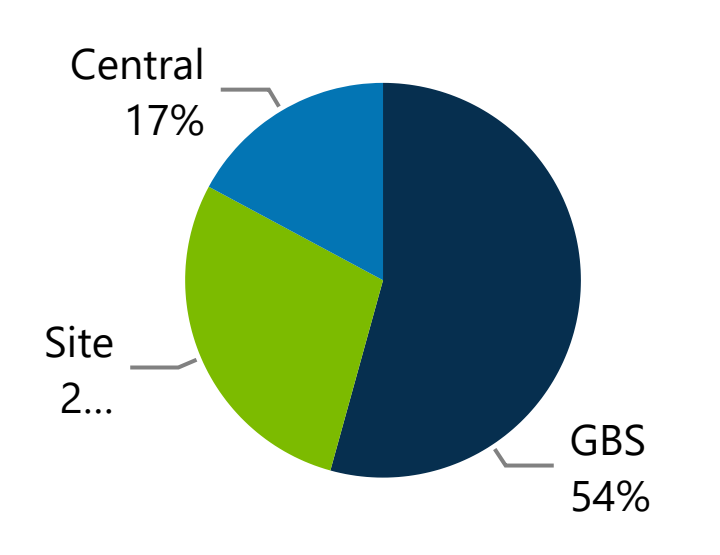

PSU Status Overview

Site	Line	Issue	Status	Due Date	Open For (Days)	Owner
Mechelen	BOTH	Comments are not copied to other DT, but reasons are. Not possible to split downtime (any kinds of DT Completed or Active) or copy the reasons to an other DT in OPS Hub for the Units.	In Progress	31-May-23	107	Ali, Yasser
Mechelen	Line 01	5/2: KPI for running scrap is counting correctly - %PRLoss scrap remains at zero. PR Rate loss contains scrap + rate loss. Scrap loss doesn't have anything linked to it and = 0.	In Progress	14-Apr-23	56	Ali, Yasser
Mechelen	Line 01	OPS HUB Close out UDE by default overdue when triggered - should be 1h to close out a run.	NOK	18-May-23	79	Ali, Yasser
Mechelen	Line01 and Unit03	NPT Admin tool: Not possible to see who edited a specific NPT or PR Out.	NOK	23-May-23	9	Ali, Yasser

Upcoming Time

5/25/2023

Status

All

Priority

All

Time Status

All

Solution

All


Open Tickets

15

Avg. Open Days


11

Priority

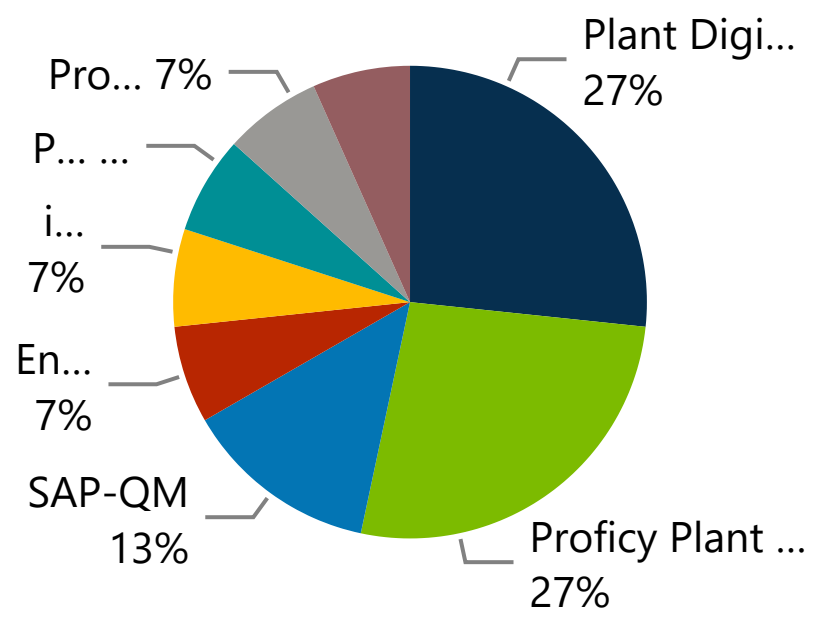

More Details

Open Tickets By Site

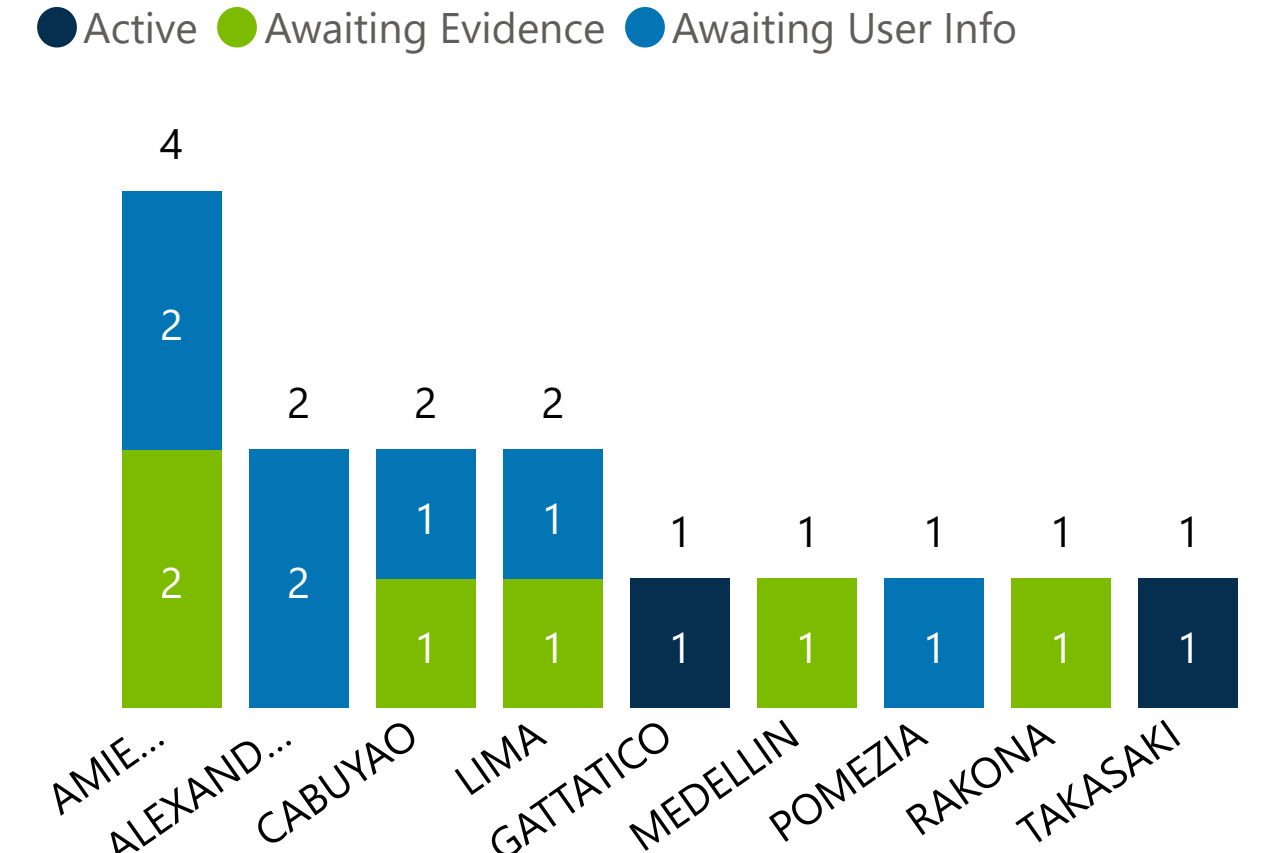

Action Items

Issues Beyond SLA

7

Within 3 Days of SLA

1

SNOW Tickets Overview									
Plant	INC	Solution	Short Description	Opened	Assigned To	Status	Priority	Diff. SLA (Days)	Beyond SLA
AMIENS	INC11172980	SAP-QM	[MFG][QM][F6P][4106] release necessary code 80751532 batch 3143030340	24-May-23	RalphJoseph Garcia	Awaiting User Info	2 - High	0.42	Yes
LIMA	INC11174000	Enovia_Proficy Web Services	FC-LIM-E2P Authentication problems with FPM to Proficy tool.	24-May-23	Gerrold Tagorda	Awaiting User Info	2 - High	0.42	Yes
CABUYAO	INC11149573	Plant Digital Platform (PDP) Thingworx	BAB-CAB-PDP-eDefects and Sharepoint List Plant Application tile's last shift filter does not reflect any of the last shift results	17-May-23	Deby Noynay	Awaiting Evidence	3 - Moderate	3.17	Yes
LIMA	INC11165125	Proficy Plant Applications	Fabric Care - LIMA (OHIO) PLANT - Converting : QA Fresh pouch strength is not saving lane 12'S results and saving the results. This test is having this issue across all converters on an infrequent basis. Tickets have been put in previously without any clear fixes in place	22-May-23	Ayush Garg	Awaiting Evidence	3 - Moderate	-1.83	No
MEDELLIN	INC11128328	Plant Digital Platform (PDP) Thingworx	BEA-MED-PDP Trigger Question are not available	11-May-23	Gerrold Tagorda	Awaiting Evidence	3 - Moderate	9.17	Yes
POMEZIA	INC11173292	Proficy Plant Applications	Fabric Care - POMEZIA PLANT & TECH CENTER - Basic : on G5 : appear 2 quality chek of the same type, but one is called "PO" , "CSO"	24-May-23	SHARANBAS AVA SHARANBAS AVA	Awaiting User Info	3 - Moderate	-3.83	No
RAKONA	INC11081631	Plant Digital Platform (PDP) Thingworx	FHC-RAK-PDP PO are not visible in AP24	27-Apr-23	RalphJoseph Garcia	Awaiting Evidence	3 - Moderate	23.17	Yes
ALEXANDRIA	INC11170236	Proficy Plant Applications	Fabric Care - ALEXANDRIA PLANT - Activity Viewer : Shiftly Centerlines for all Units on SUAL-147 and stubbing in 4 times a day instead of at the beginning of each shift. The should stub in at 0600 and	23-May-23	Sagar Hande	Awaiting User Info	4 - Low	-7.00	No
